METROMOVER UPGRADE PROJECT
STATUS DASHBOARD
SEPTEMBER 2026


ORIGINAL BASELINE SCHEDULE




CONTRACT TIME:
1460 Days

CONTRACT DAYS USED:
1460 Days

CONTRACT COMPLETION

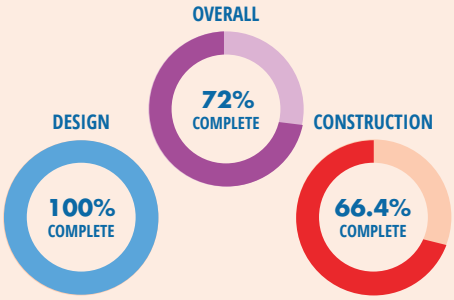

BUDGET




CONTRACT AMOUNT:
$152,920,983.22

INVOICED:
$107,220,875.60

THROUGH INVOICE 40

STATUS

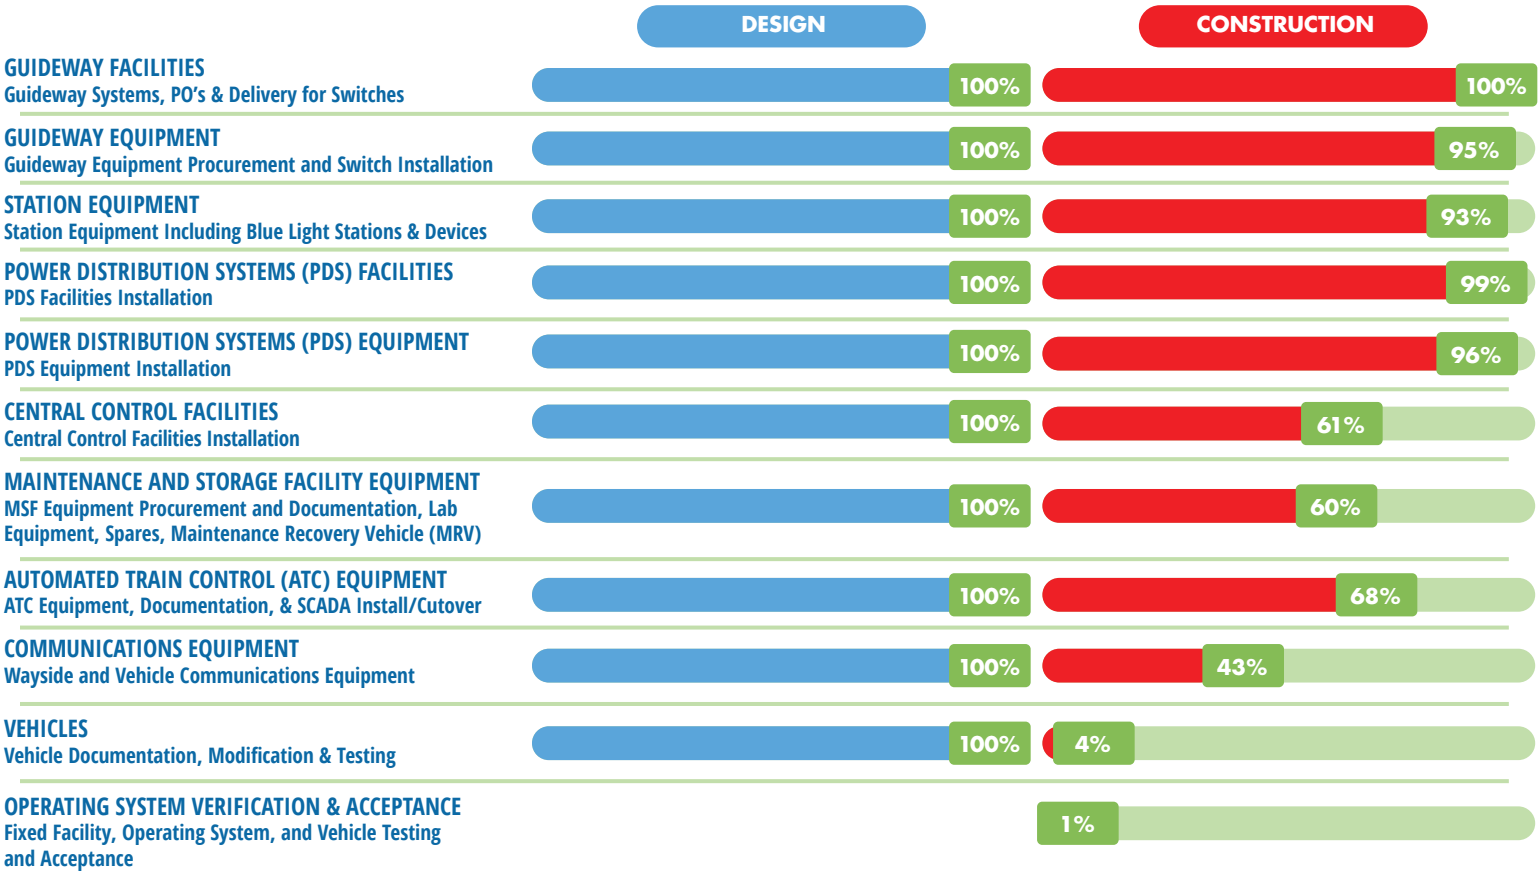

CONSTRUCTION ACTIVITIES

- Switch 56 work complete, safety certification documentation under review. Switch 55 in progress.
- Vehicle dynamic testing continues within the Omni loop, Brickell static testing in progress. Additional test vehicle certification in progress.
- Fall protection safety fencing installation ongoing.

UPCOMING LATE OPENINGS

SEPTEMBER 26, 2026	ALL LOOPS	2 P.M.
OCTOBER 10, 2026	TBD	SUN 10 P.M.
OCTOBER 24, 2026	TBD	SUN 10 P.M.

INTERACTIVE MAP DEPLOYED TO ENHANCE THE RIDERS EXPERIENCE metromoverupgrade.com

PROJECT INFORMATION
miamidade.gov/moverupgrade
786.837.4881
moverupgrade@miamidade.gov
